

WBS	Task Name	Duration	Start	Finish	Predecessors
1	**Music Streaming Platform**	**108 days**	**Mon 8/17/26**	**Fri 1/15/27**	
1.1	**Requirements and Planning**	**24 days**	**Mon 8/17/26**	**Fri 9/18/26**	
1.1.1	Hold the kickoff and elicitation meetings with the Spons	9 days	Mon 8/17/26	Thu 8/27/26	
1.1.2	Write the Software Requirements Specification (SRS)	8 days	Fri 8/28/26	Wed 9/9/26	1.1.1
1.1.3	Build the Requirements Traceability Matrix (RTM) and a	6 days	Fri 8/28/26	Mon 9/7/26	1.1.1
1.1.4	Write the Project Scope Statement, WBS and WBS Dictic	6 days	Fri 8/28/26	Mon 9/7/26	1.1.1
1.1.5	Research target users and competing apps	8 days	Mon 8/17/26	Wed 8/26/26	
1.1.6	Review the SRS, RTM and scope baseline with the Custo	2 days	Mon 9/14/26	Tue 9/15/26	1.1.2[FS+2 days],1.
1.1.7	Revise the SRS and RTM for Customer sign-off	2 days	Wed 9/16/26	Thu 9/17/26	1.1.6
1.1.8	SRS and RTM signed off by the Customer (milestone)	0 days	Fri 9/18/26	Fri 9/18/26	1.1.7[FS+1 day]
1.2	**System and Database Design**	**39 days**	**Thu 8/27/26**	**Wed 10/21/26**	
1.2.1	Evaluate the technology stack and design the system arc	8 days	Fri 8/28/26	Wed 9/9/26	1.1.1
1.2.2	Design the ER diagram and PostgreSQL schema	7 days	Mon 9/21/26	Tue 9/29/26	1.1.8
1.2.3	Design the wireframes	7 days	Thu 8/27/26	Mon 9/7/26	1.1.5
1.2.4	Design the high-fidelity mockups and clickable prototype	10 days	Mon 9/21/26	Fri 10/2/26	1.2.3,1.1.8
1.2.5	Write the detailed design (modules, class and sequence	7 days	Mon 9/21/26	Tue 9/29/26	1.2.1,1.1.8
1.2.6	Define the general API specification (OpenAPI 3.0) share	5 days	Wed 9/30/26	Tue 10/6/26	1.2.2,1.2.5
1.2.7	Set up the repository, CI/CD pipeline, staging, backups a	6 days	Tue 10/13/26	Tue 10/20/26	1.7.3[FS+2 days]
1.2.8	Review the system design and mockups with the Custon	2 days	Fri 10/9/26	Mon 10/12/26	1.2.6[FS+2 days],1.
1.2.9	Revise the mockups and prototype	3 days	Tue 10/13/26	Thu 10/15/26	1.2.8
1.2.10	Revise the system design and API specification	2 days	Mon 10/19/26	Tue 10/20/26	1.2.8,1.3.1
1.2.11	System design approved by the Customer (milestone)	0 days	Wed 10/21/26	Wed 10/21/26	1.2.9[FS+1 day],1.2
1.3	**MVP Development**	**33 days**	**Wed 10/7/26**	**Fri 11/20/26**	
1.3.1	Develop the authentication and user API with unit tests	8 days	Wed 10/7/26	Fri 10/16/26	1.2.6
1.3.2	Develop the music streaming API and CDN integration w	8 days	Wed 10/21/26	Fri 10/30/26	1.3.1,1.2.7
1.3.3	Develop the Live Premiere WebSocket service with unit	9 days	Wed 10/7/26	Mon 10/19/26	1.2.6
1.3.4	Build the playback and Live Premiere screens with unit t	10 days	Thu 10/22/26	Wed 11/4/26	1.2.11
1.3.5	Test the MVP functions (integration testing)	5 days	Thu 11/5/26	Wed 11/11/26	1.3.1,1.3.2,1.3.3,1.
1.3.6	Demo the MVP to the Customer	1 day	Thu 11/12/26	Thu 11/12/26	1.3.5
1.3.7	Fix MVP defects and demo feedback	5 days	Mon 11/16/26	Fri 11/20/26	1.3.6,1.4.1
1.3.8	MVP features completed internally (milestone)	0 days	Fri 11/20/26	Fri 11/20/26	1.3.7
1.4	**Full Feature Development**	**35 days**	**Tue 10/20/26**	**Mon 12/7/26**	
1.4.1	Develop search, playlist, library and recommendation AI	10 days	Mon 11/2/26	Fri 11/13/26	1.3.2
1.4.2	Develop favorites, comments, notification, admin and re	9 days	Tue 10/20/26	Fri 10/30/26	1.3.3
1.4.3	Build login, profile, search, recommendation, playlist, lib	10 days	Thu 11/5/26	Wed 11/18/26	1.3.4
1.4.4	Build offline download, video playback, in-app purchase	10 days	Mon 11/2/26	Fri 11/13/26	1.4.2,1.2.11
1.4.5	Test the full feature set (integration testing)	5 days	Mon 11/23/26	Fri 11/27/26	1.4.1,1.4.3,1.4.4,1.
1.4.6	Demo all functions to the Customer and Sponsor	1 day	Mon 11/30/26	Mon 11/30/26	1.4.5
1.4.7	Fix feature defects and demo feedback	5 days	Tue 12/1/26	Mon 12/7/26	1.4.6
1.4.8	All functions complete (milestone)	0 days	Mon 12/7/26	Mon 12/7/26	1.4.7
1.5	**Testing and QA**	**74 days**	**Tue 9/8/26**	**Fri 12/18/26**	
1.5.1	Write the test plan and quality metrics	5 days	Tue 9/8/26	Mon 9/14/26	1.1.3
1.5.2	Create the test case template and write the test cases fr	8 days	Mon 9/21/26	Wed 9/30/26	1.5.1,1.1.8
1.5.3	Run load (9,000-15,000 users), security and device perfc	7 days	Thu 11/12/26	Fri 11/20/26	1.3.5
1.5.4	Fix the defects found in load, security and device testing	5 days	Mon 11/23/26	Fri 11/27/26	1.5.3
1.5.5	Write the test summary report	2 days	Tue 12/8/26	Wed 12/9/26	1.5.4,1.4.7
1.5.6	Review the test summary report with the Customer	1 day	Mon 12/14/26	Mon 12/14/26	1.5.5[FS+2 days]
1.5.7	Fix the defects raised in the test review	4 days	Tue 12/15/26	Fri 12/18/26	1.5.6
1.5.8	Release candidate ready for Customer acceptance testir	0 days	Fri 12/18/26	Fri 12/18/26	1.5.7
1.6	**Deployment and Closeout**	**28 days**	**Tue 12/8/26**	**Fri 1/15/27**	
1.6.1	Deploy the release candidate to staging	2 days	Mon 12/21/26	Tue 12/22/26	1.5.8
1.6.2	Fix the defects reported by the Customer during UAT	5 days	Fri 12/25/26	Thu 12/31/26	1.6.1[FS+2 days]
1.6.3	Customer acceptance sign-off after UAT (milestone)	0 days	Mon 1/4/27	Mon 1/4/27	1.6.2[FS+1 day]
1.6.4	Deploy to production with monitoring and backups	3 days	Tue 1/5/27	Thu 1/7/27	1.6.3
1.6.5	Provide post-release hypercare	6 days	Fri 1/8/27	Fri 1/15/27	1.6.4
1.6.6	Submit the apps to the App Store and Google Play	2 days	Fri 1/8/27	Mon 1/11/27	1.6.4
1.6.7	Train the Customer administrators	2 days	Tue 1/12/27	Wed 1/13/27	1.6.6
1.6.8	Write the user guide, admin guide and release notes (Vi	10 days	Tue 12/8/26	Mon 12/21/26	1.4.7
1.6.9	Write the deployment and operations documentation	7 days	Wed 12/23/26	Thu 12/31/26	1.6.1
1.6.10	Review the handover deliverables with the Customer	2 days	Wed 1/6/27	Thu 1/7/27	1.6.8[FS+2 days],1.
1.6.11	Revise the handover documents	3 days	Fri 1/8/27	Tue 1/12/27	1.6.10
1.6.12	Apps published and deliverables handed over (milestone	0 days	Fri 1/15/27	Fri 1/15/27	1.6.6[FS+3 days],1.
1.7	**Project Management**	**90 days**	**Fri 9/11/26**	**Fri 1/15/27**	
1.7.1	Develop the Project Management Plan (schedule, cost b	10 days	Wed 9/16/26	Tue 9/29/26	1.1.6
1.7.2	Project Management Plan approved by the Sponsor (mil	0 days	Thu 10/1/26	Thu 10/1/26	1.7.1[FS+2 days]
1.7.3	Procure the cloud, CDN, test devices and test tools	5 days	Fri 10/2/26	Thu 10/8/26	1.7.2
1.7.4	**Track progress and send status and cost reports to the**	**90 days**	**Fri 9/11/26**	**Fri 1/15/27**	
1.7.4.1	Track progress and send the Month 1 status and cost	1 day	Fri 9/11/26	Fri 9/11/26	1.1.1
1.7.4.2	Track progress and send the Month 2 status and cost	2 days	Thu 10/15/26	Fri 10/16/26	1.7.4.1,1.7.2
1.7.4.3	Track progress and send the Month 3 status and cost	2 days	Fri 11/13/26	Mon 11/16/26	1.7.4.2
1.7.4.4	Track progress and send the Month 4 status and cost	2 days	Thu 12/10/26	Fri 12/11/26	1.7.4.3
1.7.4.5	Track progress and send the Month 5 status and cost	2 days	Thu 1/14/27	Fri 1/15/27	1.7.4.4
1.7.5	**Monitor risks and manage change requests**	**65 days**	**Wed 10/14/26**	**Wed 1/13/27**	
1.7.5.1	Review risks and change requests (review 1 of 8)	1 day	Wed 10/14/26	Wed 10/14/26	1.7.2
1.7.5.2	Review risks and change requests (review 2 of 8)	1 day	Wed 10/28/26	Wed 10/28/26	1.7.5.1
1.7.5.3	Review risks and change requests (review 3 of 8)	1 day	Wed 11/11/26	Wed 11/11/26	1.7.5.2
1.7.5.4	Review risks and change requests (review 4 of 8)	1 day	Wed 11/25/26	Wed 11/25/26	1.7.5.3
1.7.5.5	Review risks and change requests (review 5 of 8)	1 day	Wed 12/9/26	Wed 12/9/26	1.7.5.4
1.7.5.6	Review risks and change requests (review 6 of 8)	1 day	Wed 12/23/26	Wed 12/23/26	1.7.5.5
1.7.5.7	Review risks and change requests (review 7 of 8)	1 day	Tue 1/5/27	Tue 1/5/27	1.7.5.6
1.7.5.8	Review risks and change requests (review 8 of 8, final	1 day	Wed 1/13/27	Wed 1/13/27	1.7.5.7
1.7.6	Collect lessons learned and write the final project repor	5 days	Tue 12/15/26	Mon 12/21/26	1.5.6
1.7.7	Review the final project report with the Sponsor	1 day	Fri 1/8/27	Fri 1/8/27	1.7.6[FS+2 days],1.
1.7.8	Revise the final report and close the project	2 days	Mon 1/11/27	Tue 1/12/27	1.7.7
1.7.9	Project closed with Sponsor sign-off (milestone)	0 days	Fri 1/15/27	Fri 1/15/27	1.7.8,1.6.12,1.7.4.5

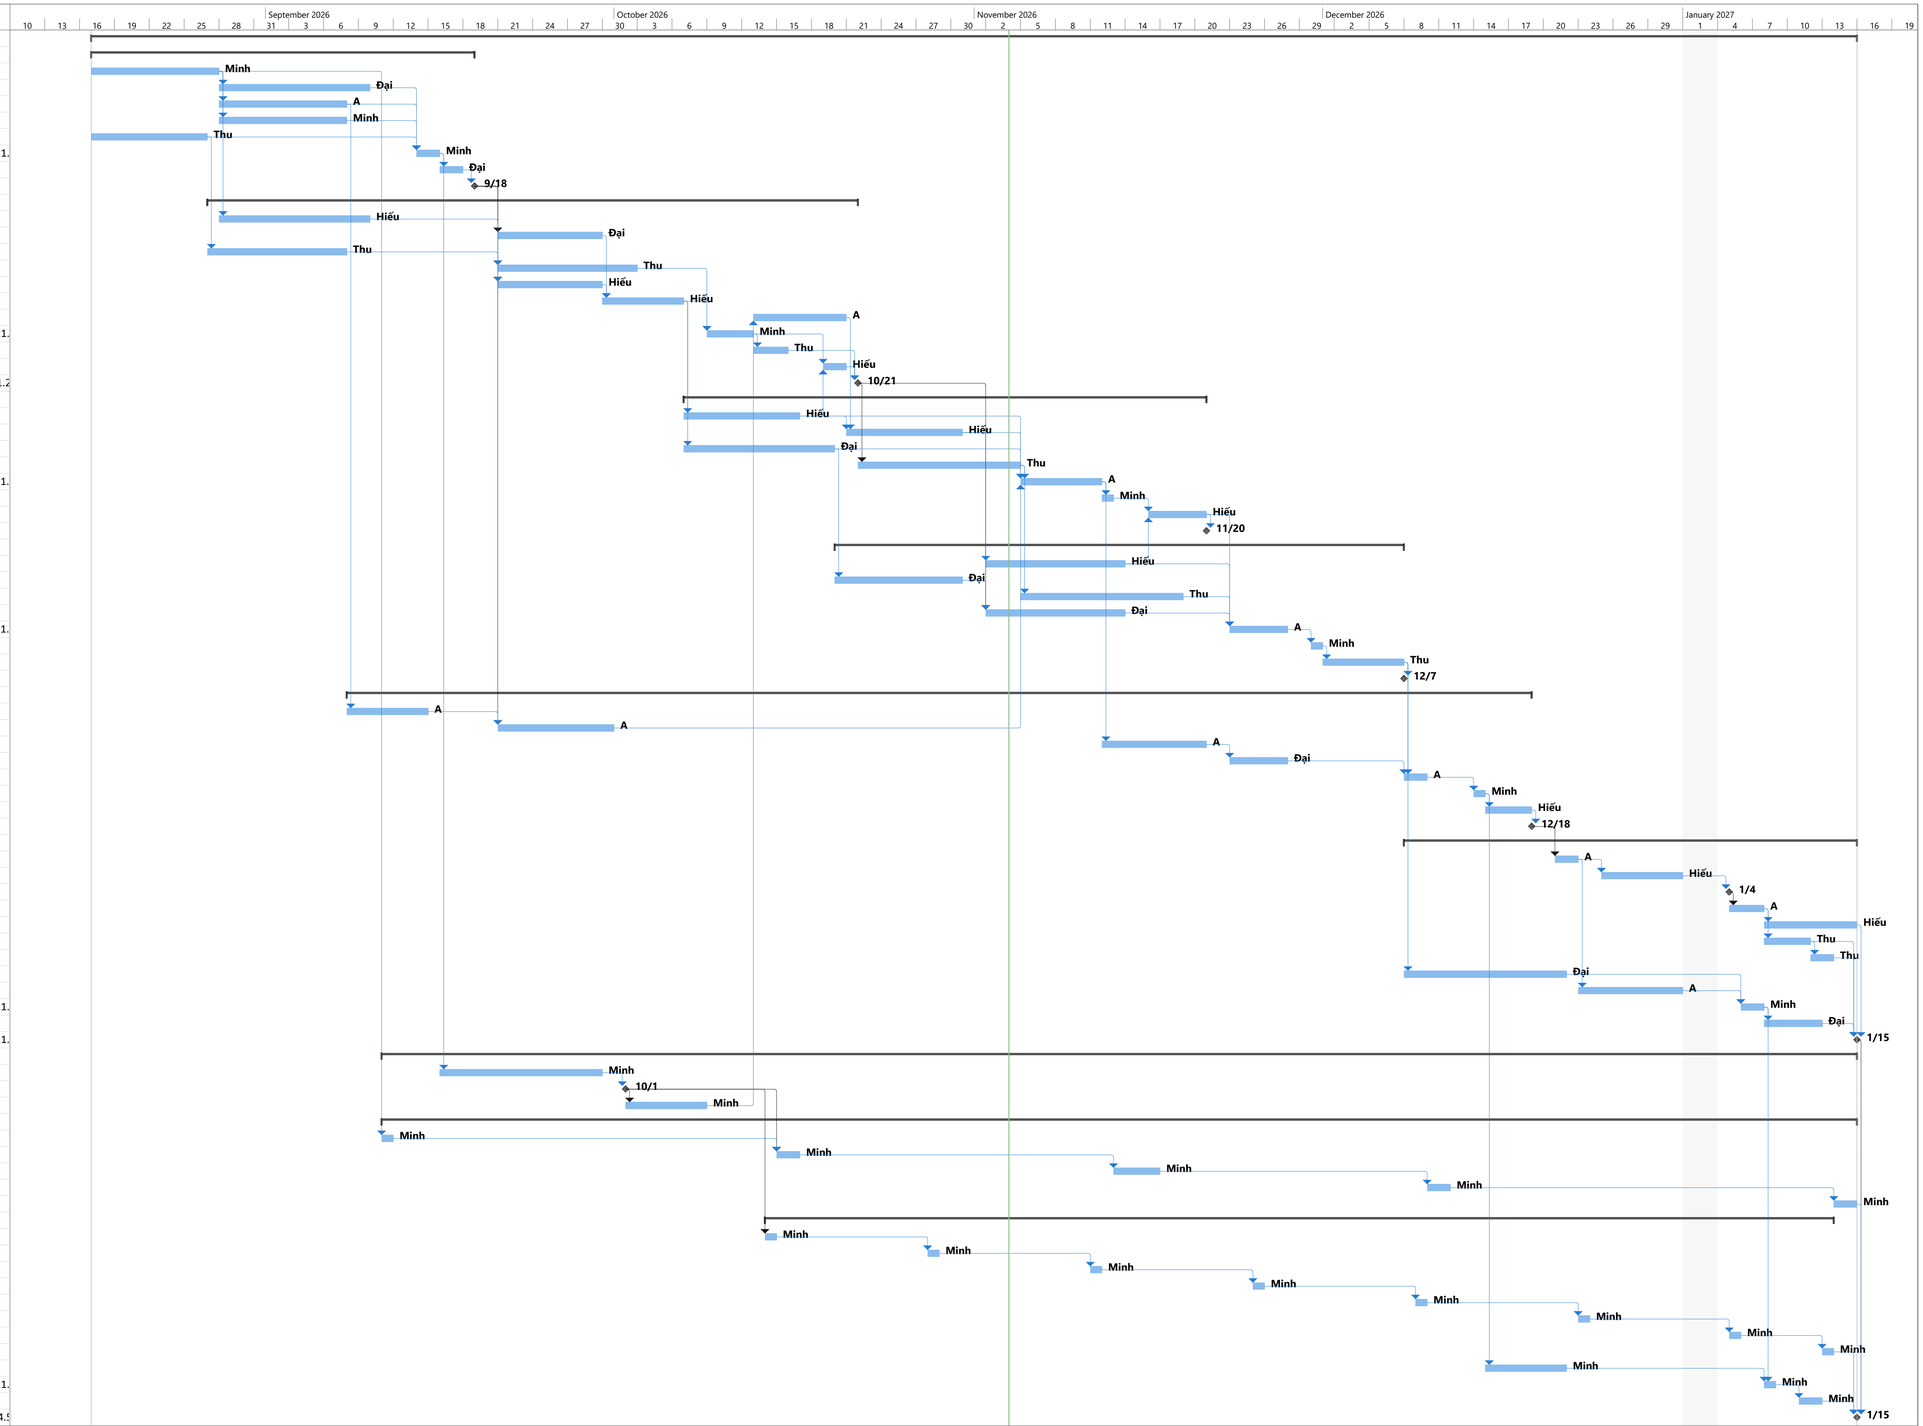

Project: Development and Depl
Date: Wed 11/4/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

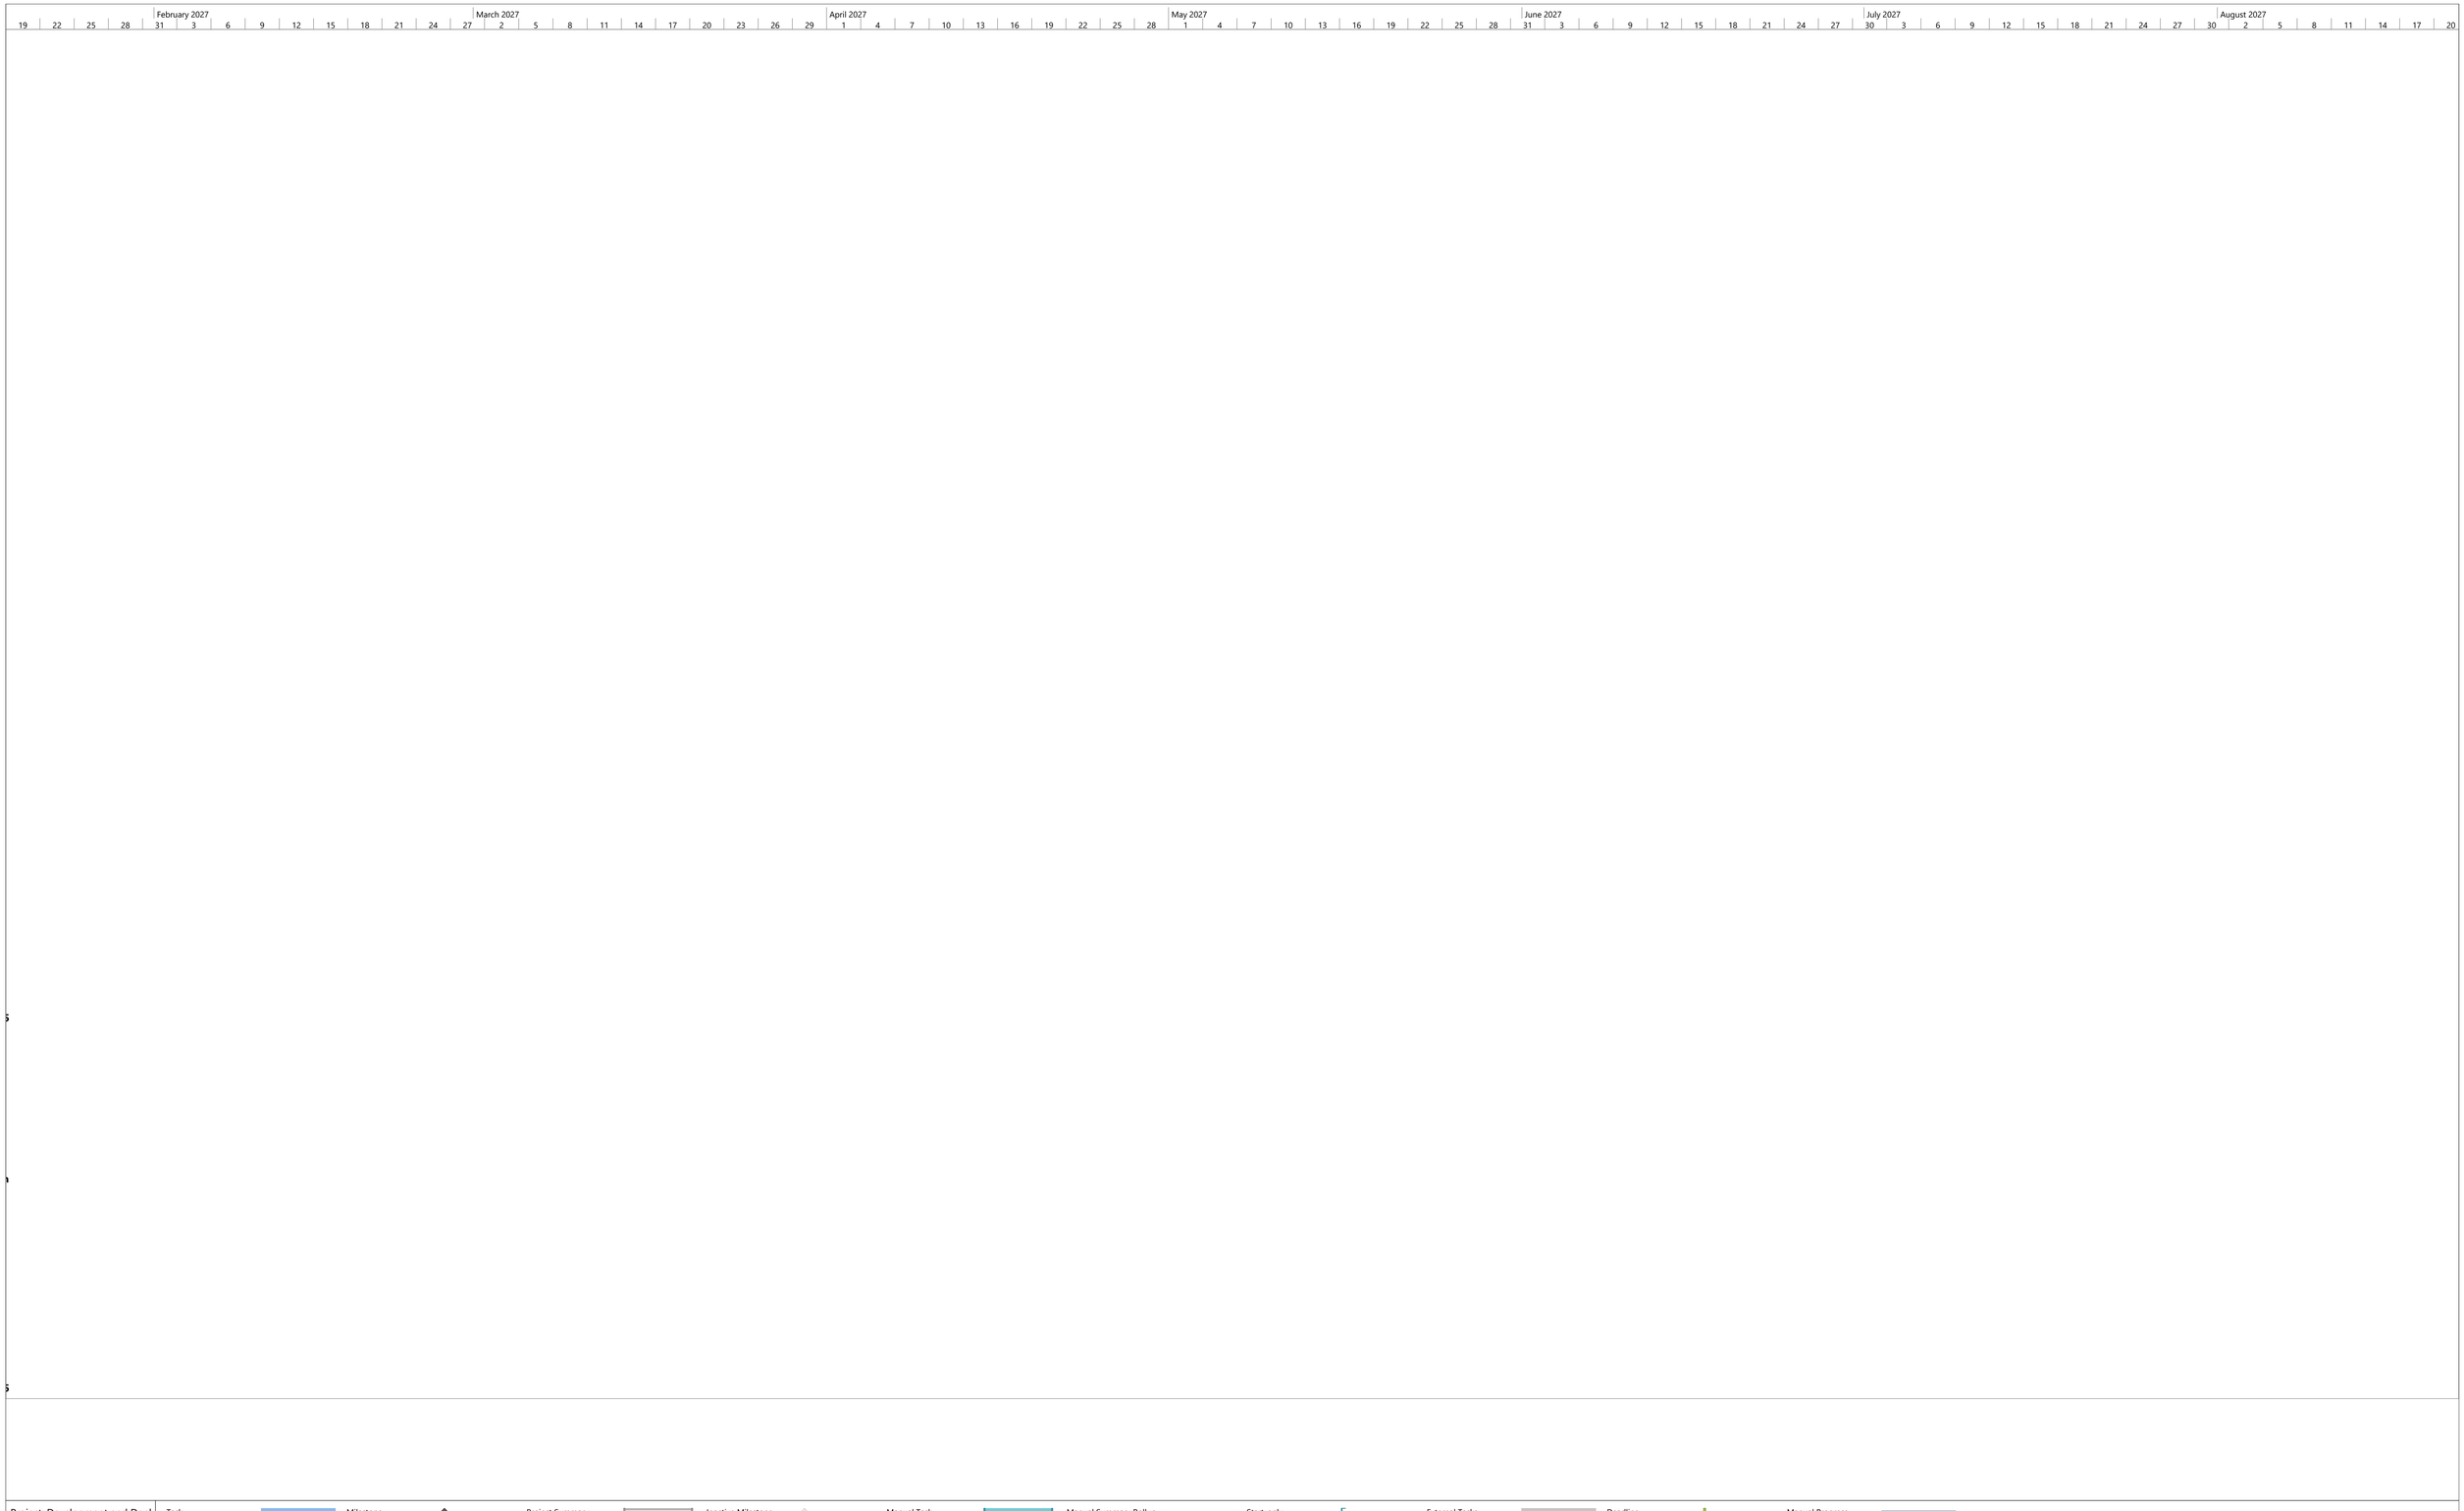

Project: Development and Depl
Date: Wed 11/4/26

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
