

WBS	Task Name	Duration	Start	Finish
1	**Music Streaming Platform**	**108 days**	**Mon 8/17/26**	**Fri 1/15/27**
1.1	**Requirements and Planning**	**24 days**	**Mon 8/17/26**	**Fri 9/18/26**
1.1.1	Hold elicitation meetings and write the Chart	9 days	Mon 8/17/26	Thu 8/27/26
1.1.2	Write the SRS	8 days	Fri 8/28/26	Wed 9/9/26
1.1.3	Build the RTM and acceptance criteria	6 days	Fri 8/28/26	Mon 9/7/26
1.1.4	Write the Scope Statement, WBS, WBS Dictic	6 days	Fri 8/28/26	Mon 9/7/26
1.1.5	Research target users and competing apps	8 days	Mon 8/17/26	Wed 8/26/26
1.1.6	Review the SRS and RTM with Customer and	2 days	Mon 9/14/26	Tue 9/15/26
1.1.7	Revise the SRS and RTM	2 days	Wed 9/16/26	Thu 9/17/26
1.1.8	SRS and RTM signed off (milestone)	0 days	Fri 9/18/26	Fri 9/18/26
1.2	**System and Database Design**	**39 days**	**Thu 8/27/26**	**Wed 10/21/26**
1.2.1	Design the system architecture	8 days	Fri 8/28/26	Wed 9/9/26
1.2.2	Design the database (ER diagram, schema)	7 days	Mon 9/21/26	Tue 9/29/26
1.2.3	Design the wireframes	7 days	Thu 8/27/26	Mon 9/7/26
1.2.4	Design the mockups and prototype	10 days	Mon 9/21/26	Fri 10/2/26
1.2.5	Write the detailed design	7 days	Mon 9/21/26	Tue 9/29/26
1.2.6	Define the general API specification	5 days	Wed 9/30/26	Tue 10/6/26
1.2.7	Set up the repository, CI/CD, staging and CDN	6 days	Tue 10/13/26	Tue 10/20/26
1.2.8	Review the design with the Customer	2 days	Fri 10/9/26	Mon 10/12/26
1.2.9	Revise the mockups and prototype	3 days	Tue 10/13/26	Thu 10/15/26
1.2.10	Revise the design and API specification	2 days	Mon 10/19/26	Tue 10/20/26
1.2.11	Design approved by the Customer (milestone	0 days	Wed 10/21/26	Wed 10/21/26
1.3	**MVP Development**	**33 days**	**Wed 10/7/26**	**Fri 11/20/26**
1.3.1	Develop the authentication and user API	8 days	Wed 10/7/26	Fri 10/16/26
1.3.2	Develop the streaming API and CDN integrati	8 days	Wed 10/21/26	Fri 10/30/26
1.3.3	Develop the Live Premiere WebSocket servic	9 days	Wed 10/7/26	Mon 10/19/26
1.3.4	Build the playback and Live Premiere screens	10 days	Thu 10/22/26	Wed 11/4/26
1.3.5	Test the MVP (integration testing)	5 days	Thu 11/5/26	Wed 11/11/26
1.3.6	Demo the MVP to the Customer	1 day	Thu 11/12/26	Thu 11/12/26
1.3.7	Fix MVP defects and demo feedback	5 days	Mon 11/16/26	Fri 11/20/26
1.3.8	MVP completed internally (milestone)	0 days	Fri 11/20/26	Fri 11/20/26
1.4	**Full Feature Development**	**35 days**	**Tue 10/20/26**	**Mon 12/7/26**
1.4.1	Develop the discovery and library APIs	10 days	Mon 11/2/26	Fri 11/13/26
1.4.2	Develop social, notification, admin and receip	9 days	Tue 10/20/26	Fri 10/30/26
1.4.3	Build account, discovery, library and social sc	10 days	Thu 11/5/26	Wed 11/18/26
1.4.4	Build download, video, purchase and admin s	10 days	Mon 11/2/26	Fri 11/13/26
1.4.5	Test all functions (integration testing)	5 days	Mon 11/23/26	Fri 11/27/26
1.4.6	Demo all functions to Customer and Sponsor	1 day	Mon 11/30/26	Mon 11/30/26
1.4.7	Fix feature defects and demo feedback	5 days	Tue 12/1/26	Mon 12/7/26
1.4.8	All functions complete (milestone)	0 days	Mon 12/7/26	Mon 12/7/26
1.5	**Testing and QA**	**74 days**	**Tue 9/8/26**	**Fri 12/18/26**
1.5.1	Write the test plan and quality metrics	5 days	Tue 9/8/26	Mon 9/14/26
1.5.2	Create the test case template and test cases	8 days	Mon 9/21/26	Wed 9/30/26
1.5.3	Run load, security and device tests	7 days	Thu 11/12/26	Fri 11/20/26
1.5.4	Fix load, security and device test defects	5 days	Mon 11/23/26	Fri 11/27/26
1.5.5	Write the test summary report	2 days	Tue 12/8/26	Wed 12/9/26
1.5.6	Review the test report with the Customer	1 day	Mon 12/14/26	Mon 12/14/26
1.5.7	Fix the test review defects	4 days	Tue 12/15/26	Fri 12/18/26
1.5.8	Release candidate ready for UAT (milestone)	0 days	Fri 12/18/26	Fri 12/18/26
1.6	**Deployment and Closeout**	**28 days**	**Tue 12/8/26**	**Fri 1/15/27**
1.6.1	Deploy the release candidate to staging	2 days	Mon 12/21/26	Tue 12/22/26
1.6.2	Fix the defects reported in UAT	5 days	Fri 12/25/26	Thu 12/31/26
1.6.3	Customer acceptance sign-off (milestone)	0 days	Mon 1/4/27	Mon 1/4/27
1.6.4	Deploy to production	3 days	Tue 1/5/27	Thu 1/7/27
1.6.5	Provide post-release hypercare	6 days	Fri 1/8/27	Fri 1/15/27
1.6.6	Submit the apps to App Store and Google Pla	2 days	Fri 1/8/27	Mon 1/11/27
1.6.7	Train the Customer administrators	2 days	Tue 1/12/27	Wed 1/13/27
1.6.8	Write the user and admin guides, release not	10 days	Tue 12/8/26	Mon 12/21/26
1.6.9	Write the deployment and operations guide	7 days	Wed 12/23/26	Thu 12/31/26
1.6.10	Review the handover with the Customer	2 days	Wed 1/6/27	Thu 1/7/27
1.6.11	Revise the handover documents	3 days	Fri 1/8/27	Tue 1/12/27
1.6.12	Apps published and handed over (milestone)	0 days	Fri 1/15/27	Fri 1/15/27
1.7	**Project Management**	**90 days**	**Fri 9/11/26**	**Fri 1/15/27**
1.7.1	Develop the Project Management Plan	10 days	Wed 9/16/26	Tue 9/29/26
1.7.2	Project Management Plan approved (milesto	0 days	Thu 10/1/26	Thu 10/1/26
1.7.3	Procure cloud, CDN, devices and test tools	5 days	Fri 10/2/26	Thu 10/8/26
1.7.4	**Track progress and report status and cost**	**90 days**	**Fri 9/11/26**	**Fri 1/15/27**
1.7.4.1	Report Month 1 status and cost	1 day	Fri 9/11/26	Fri 9/11/26
1.7.4.2	Report Month 2 status and cost	2 days	Thu 10/15/26	Fri 10/16/26
1.7.4.3	Report Month 3 status and cost	2 days	Fri 11/13/26	Mon 11/16/26
1.7.4.4	Report Month 4 status and cost	2 days	Thu 12/10/26	Fri 12/11/26
1.7.4.5	Report Month 5 status and cost	2 days	Thu 1/14/27	Fri 1/15/27
1.7.5	**Monitor risks and manage change requests**	**65 days**	**Wed 10/14/26**	**Wed 1/13/27**
1.7.5.1	Review risks and changes (1 of 8)	1 day	Wed 10/14/26	Wed 10/14/26
1.7.5.2	Review risks and changes (2 of 8)	1 day	Wed 10/28/26	Wed 10/28/26
1.7.5.3	Review risks and changes (3 of 8)	1 day	Wed 11/11/26	Wed 11/11/26
1.7.5.4	Review risks and changes (4 of 8)	1 day	Wed 11/25/26	Wed 11/25/26
1.7.5.5	Review risks and changes (5 of 8)	1 day	Wed 12/9/26	Wed 12/9/26
1.7.5.6	Review risks and changes (6 of 8)	1 day	Wed 12/23/26	Wed 12/23/26
1.7.5.7	Review risks and changes (7 of 8)	1 day	Tue 1/5/27	Tue 1/5/27
1.7.5.8	Review risks and changes (8 of 8, final)	1 day	Wed 1/13/27	Wed 1/13/27
1.7.6	Write the lessons learned and final report	5 days	Tue 12/15/26	Mon 12/21/26
1.7.7	Review the final report with the Sponsor	1 day	Fri 1/8/27	Fri 1/8/27
1.7.8	Revise the final report and close the project	2 days	Mon 1/11/27	Tue 1/12/27
1.7.9	Project closed by the Sponsor (milestone)	0 days	Fri 1/15/27	Fri 1/15/27

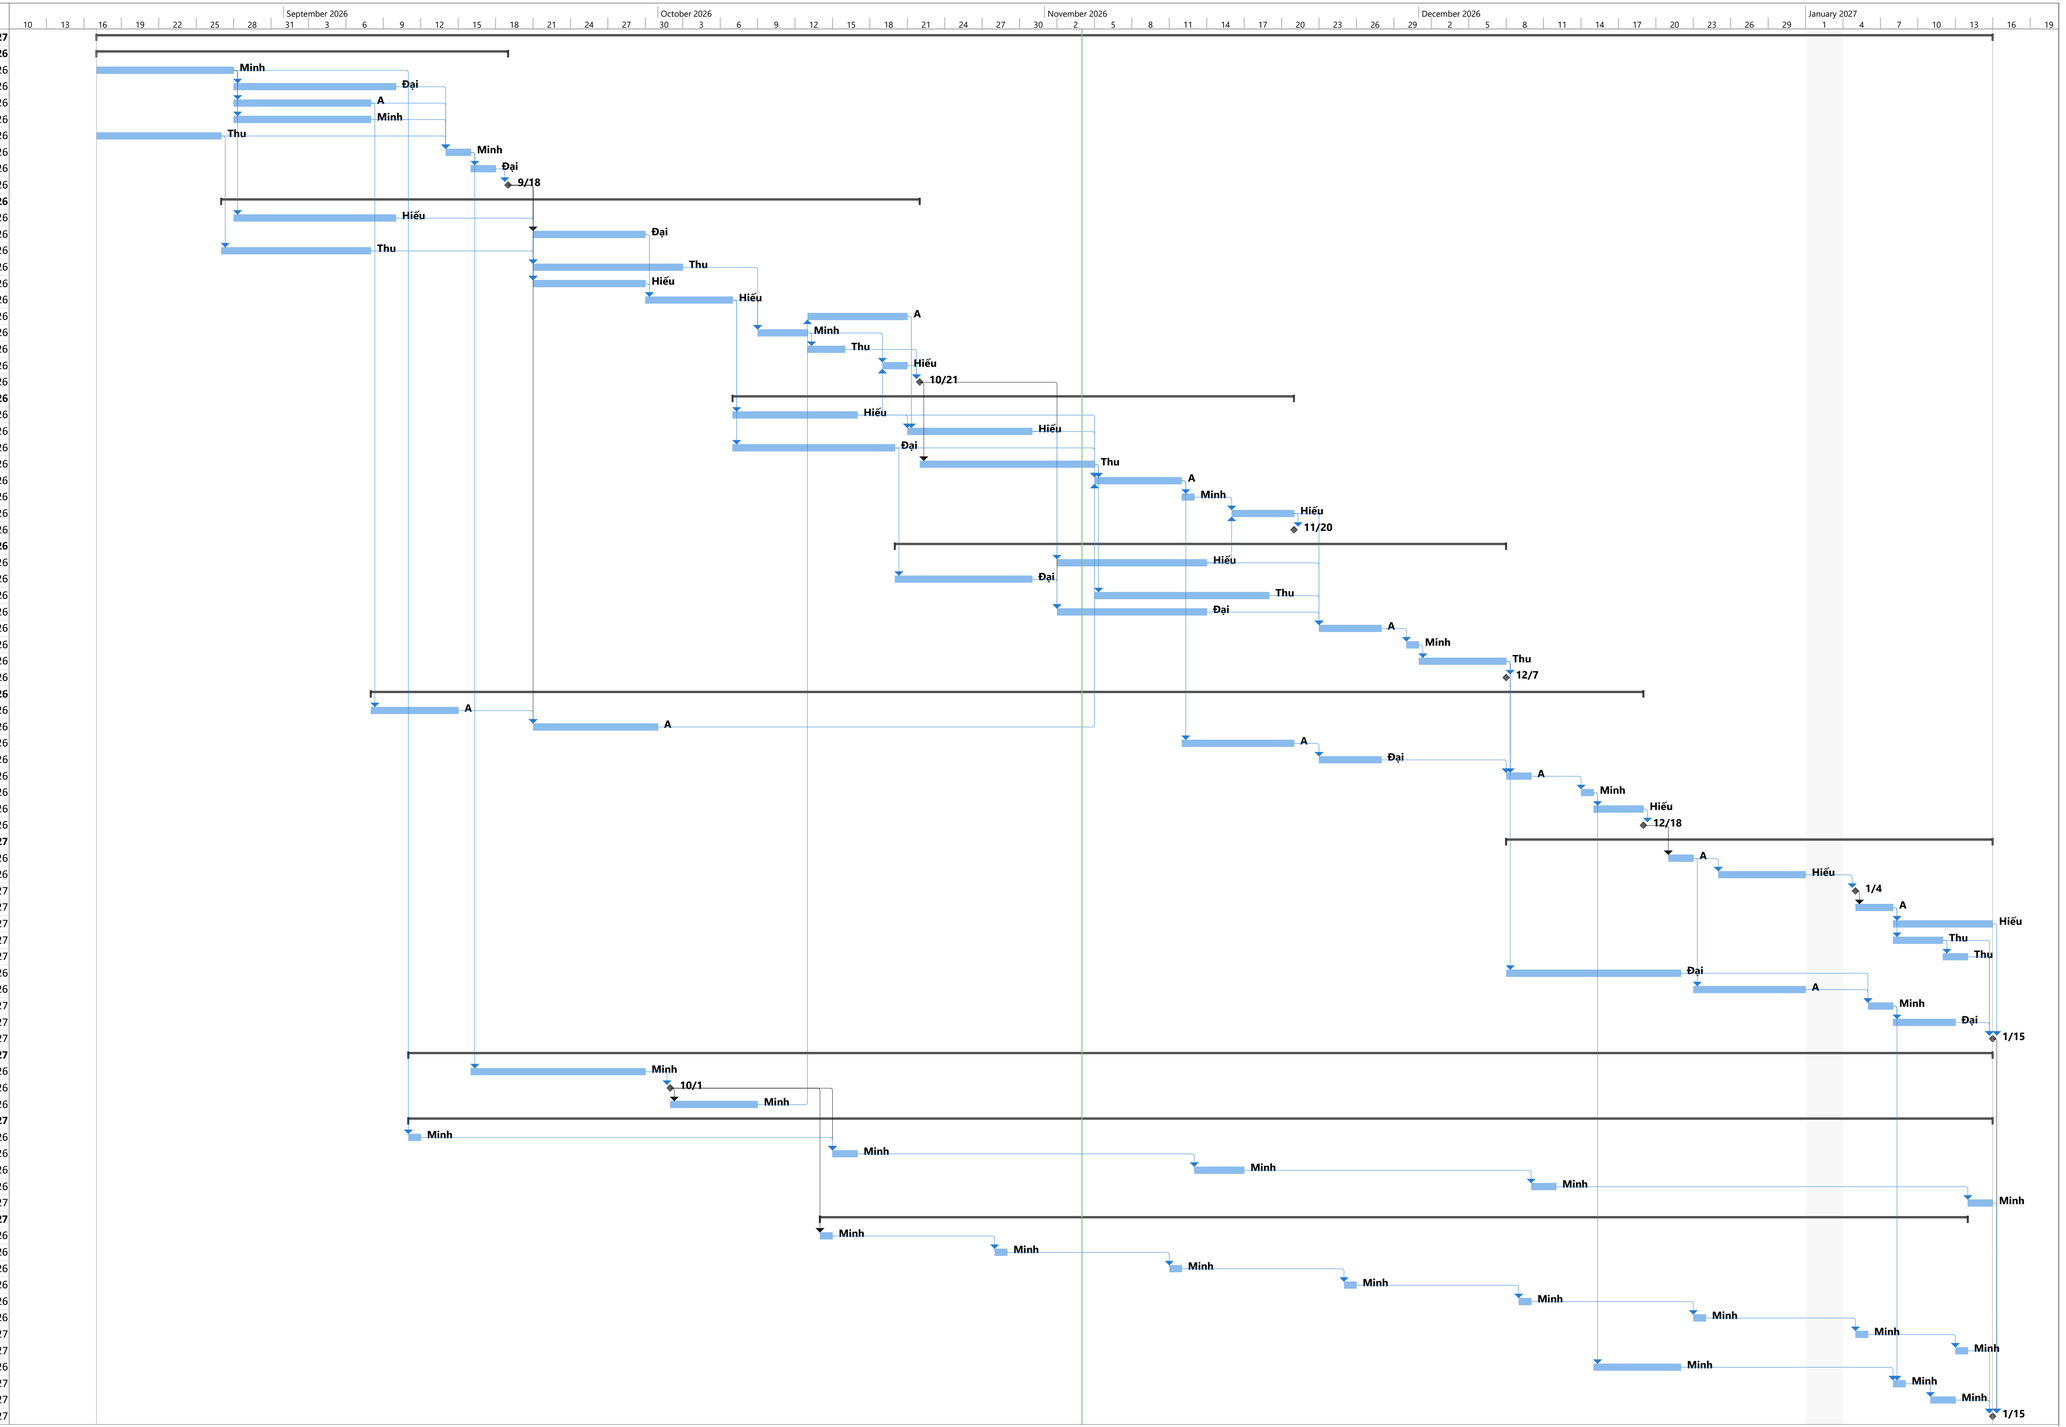

Project: Development and Depl
Date: Wed 11/4/26

Task | Milestone | Project Summary | Inactive Milestone | Manual Task | Manual Summary Rollup | Start-only | External Tasks | Deadline | Manual Progress
Split | Summary | Inactive Task | Inactive Summary | Duration-only | Manual Summary | Finish-only | External Milestone | Progress

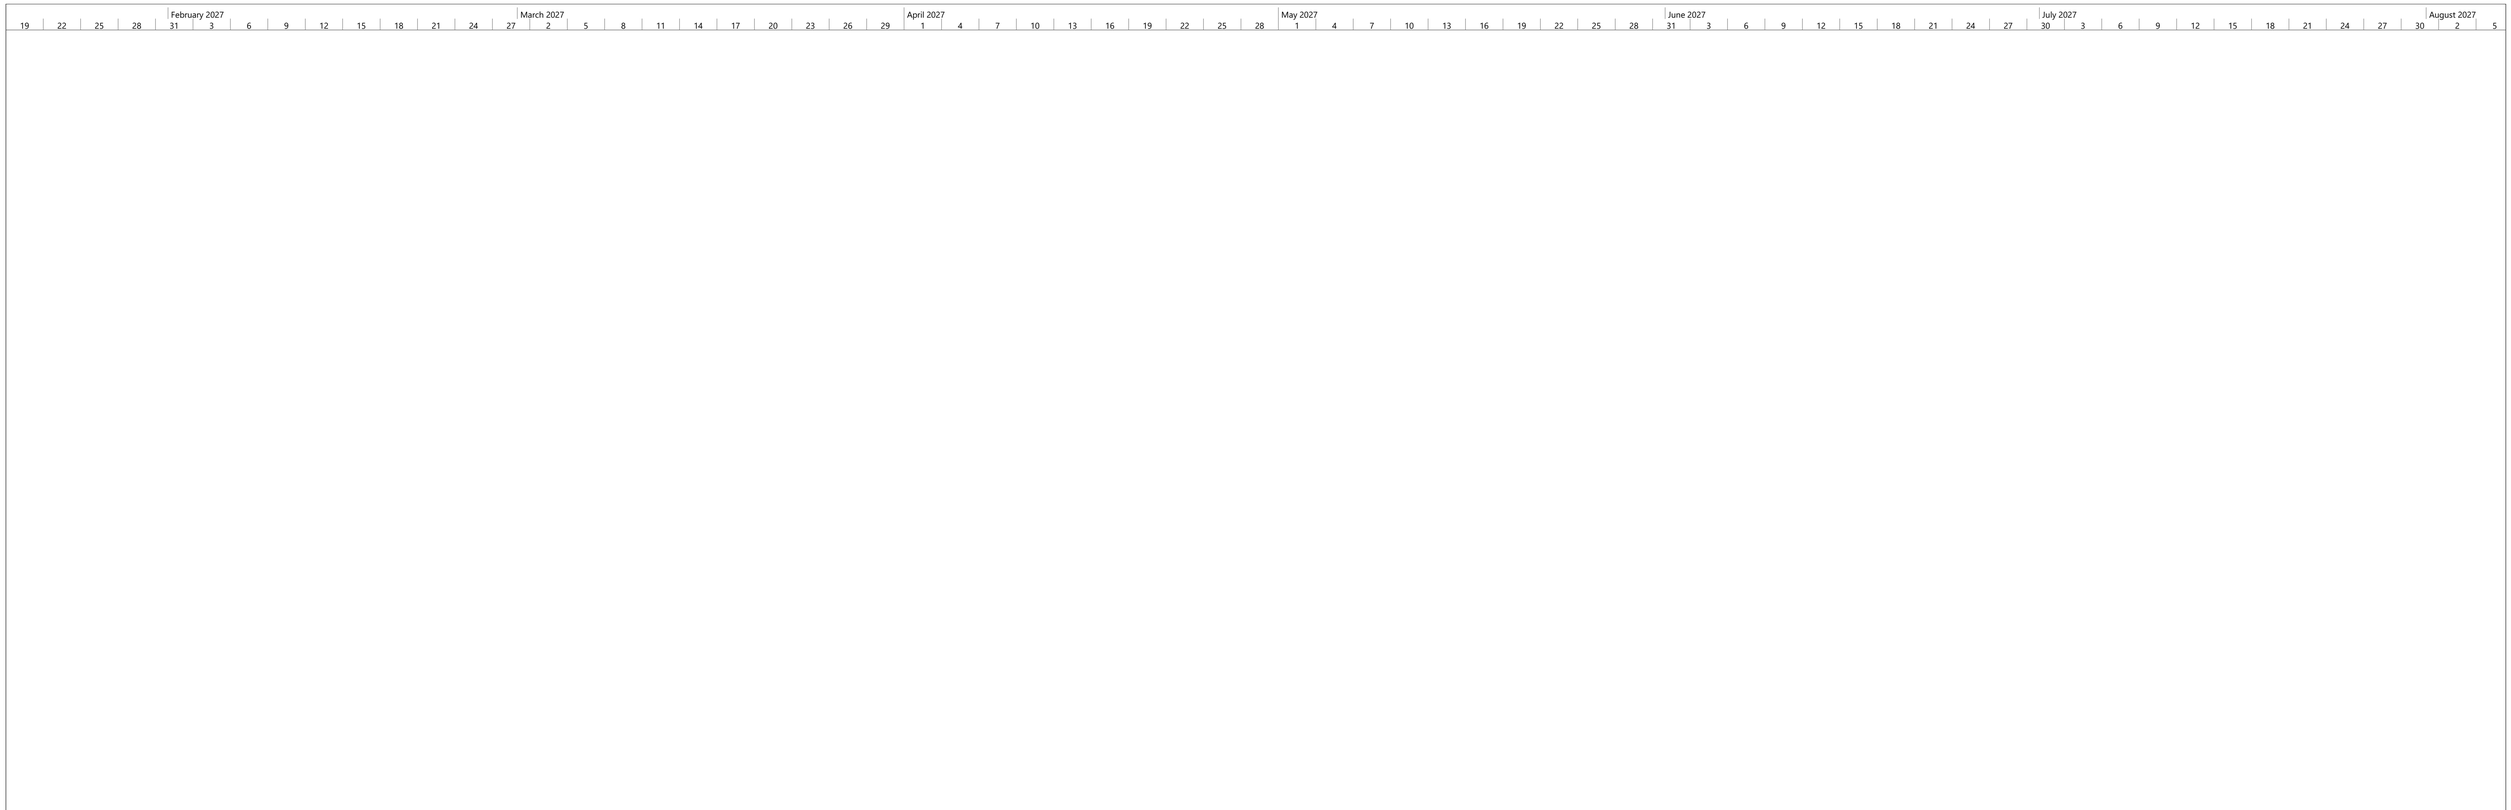

Project: Development and Depl
Date: Wed 11/4/26

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
